RBP ORC Pipeline - Conceptual Schedule
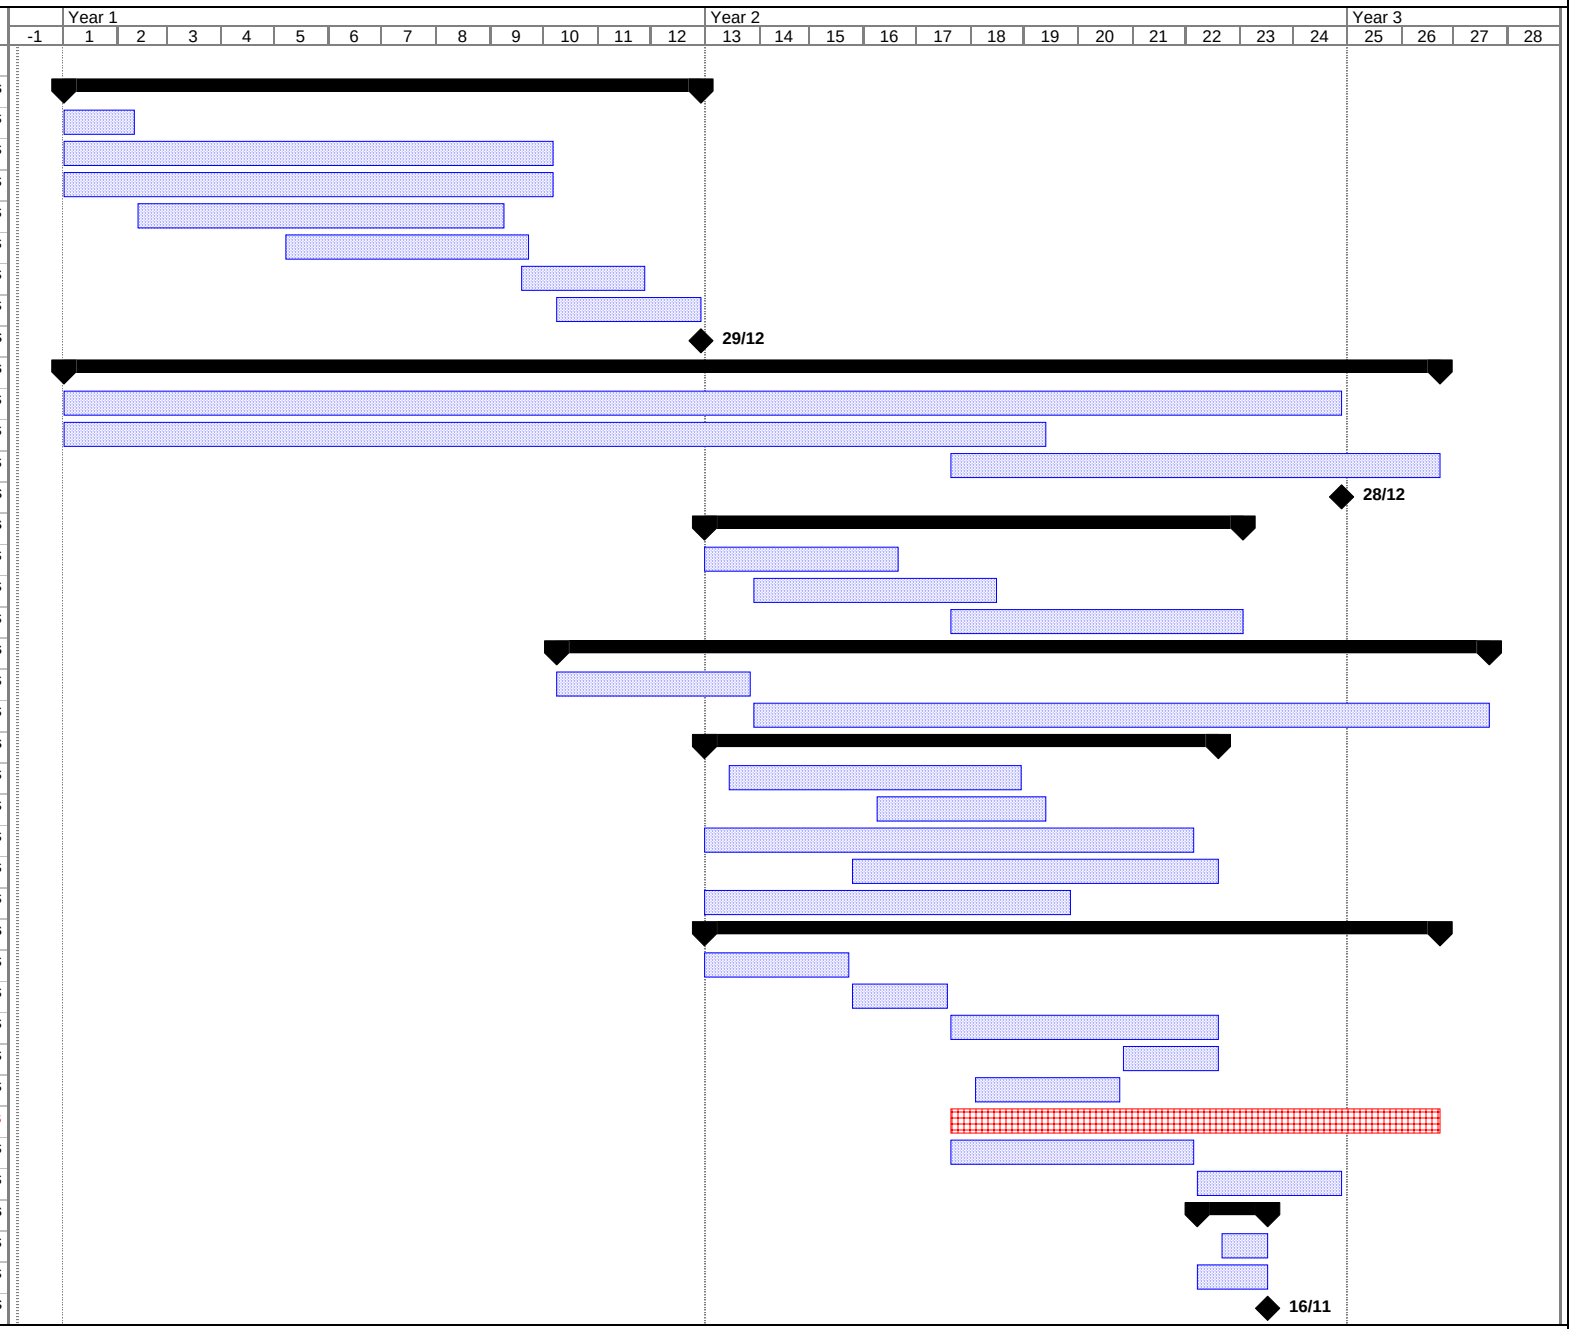
ID	Task Name	Duration
1		
2	**Project Approvals**	**260 days**
3	Licence Application	6 wks
4	Land Acquisition	40 wks
5	Environmental Studies	40 wks
6	Cultural Heritage Studies	30 wks
7	Design Basis & Planning	20 wks
8	Long Lead Materials	10 wks
9	Review and Approve	12 wks
10	Licence Grant	0 days
11	**Project Management**	**560 days**
12	Management	104 wks
13	Contract Management	80 wks
14	As-Built and Closeout	40 wks
15	Project Complete	0 days
16	**Engineering**	**220 days**
17	Detail Pipeline Design	16 wks
18	Station Detail Design	20 wks
19	Engineering Through Const	24 wks
20	**Land Management**	**380 days**
21	Land Acquisition	16 wks
22	Management and Closeout	60 wks
23	**Materials**	**210 days**
24	Pipe	24 wks
25	Coating	14 wks
26	Compressors	40 wks
27	Station Materials	30 wks
28	Other	30 wks
29	**Construction**	**300 days**
30	Tendering	12 wks
31	Mobilisation	8 wks
32	Wallumbilla -Haigslea	22 wks
33	Haigslea-Swanbank	8 wks
34	Swanbank-Gibson Island	12 wks
35	**Existing Route**	**40 wks**
36	Stations	20 wks
37	Punchlist Closeout	12 wks
38	**Commissioning**	**30 days**
39	Pipeline	4 wks
40	Stations	6 wks
41	First Gas	0 days
